



# State Park Road Reconstruction Project

**Welcome!**

**Public Meeting No. 5**

**January 23, 2020**



Robert Peccia & Associates – Kalispell, Montana





# State Park Road Reconstruction Project

## □ Project Contacts

### ▣ City of Whitefish

- Craig Workman, PE, Public Works Director
- Karin Hilding, PE, Senior City Engineer
- Jenny Emmenegger, Office Manager

### ▣ Robert Peccia & Associates (RPA) – Consulting Engineers

- Brandon Theis, PE, Project Manager
- Bill Bell, EI, Designer & Construction Tech.
- Ryan Mitchell, PE, PLS, Kalispell Operations Manager



Robert Peccia & Associates – Kalispell, Montana





# State Park Road Reconstruction Project

- **Phase 1 (Lion Mountain Loop to Haugen Heights)**
  - ▣ Complete!
- **Phase 2 (Haugen Heights to Railroad Tracks)**
  - ▣ Project Schedule
  - ▣ Patton/Lake Park Intersection Changes
  - ▣ Detour Plans
  - ▣ Mail Delivery during Construction
  - ▣ Public Communication (sign-in sheet and comment sheets)





## PHASE 2 –HAUGEN HEIGHTS TO RAILROAD CROSSING

Spring  
2020

- Advertising, Bidding & Contractor Selection
- Begin Construction (April thru June)
- Construction Detours

Summer  
2020

- Construction of Private Utilities (July thru August)
- No work over July 4<sup>th</sup> and Labor Day weekends
- Construction Detour “A”

Fall  
2020

- Finish Construction (September thru November)
- Construction Detours



# State Park Road Reconstruction Project

## □ Phase 2 Construction Schedule for 2020

### □ April thru June (City Contractor):

- Complete City Utilities (water, sewer, storm, utilizing Detour A).
- Complete Haugen Heights Intersection (Detour B).
- Place gravel driving surface with dust abatement for summer traffic.

### □ July thru August (Private Utility Contractors):

- Complete Private Utilities (gas, power, fiber, utilizing Detour A).

### □ September thru November (City Contractor):


- Complete Remaining Roadway Improvements (sidewalks, asphalt, street lights, etc.).





# Patton/Lake Park Intersection Changes


- ❑ “Old” State Park Road (north of Lake Park Lane) to become Patton Lane.
- ❑ Will change 5 addresses from “State Park Road” to “Patton Lane”.
- ❑ Public Hearing scheduled for March 2, 2020 during City Council Meeting.

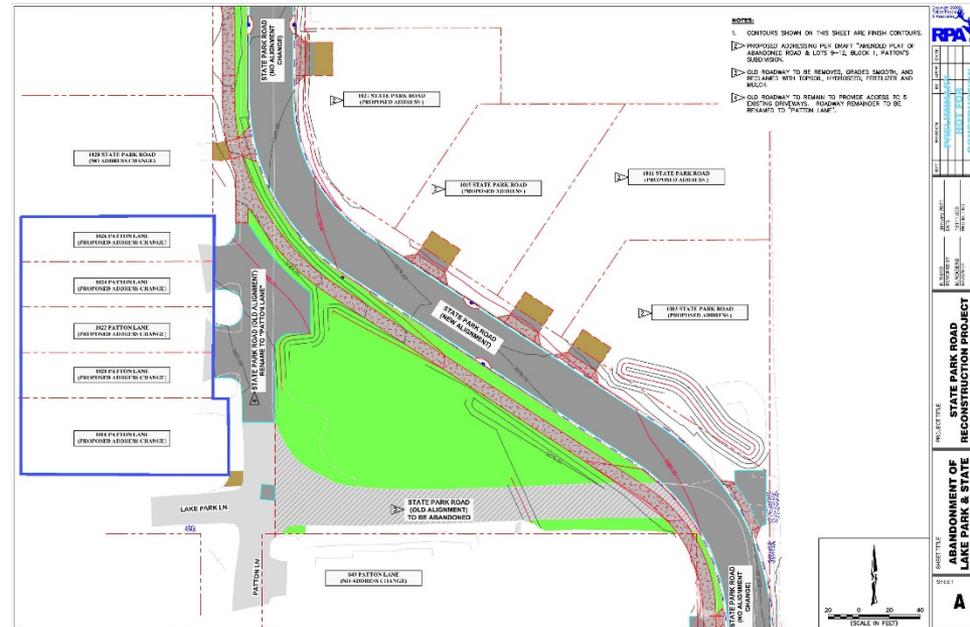



## Detour "A"


- Detour "A" will be implemented during the majority of the project.
- Daytime travel: 2-way, 1-lane traffic with flaggers or 2-way, 2-lane traffic.
- Expect delays.
- Evening/Weekend travel: 2-way, 2-lane traffic.

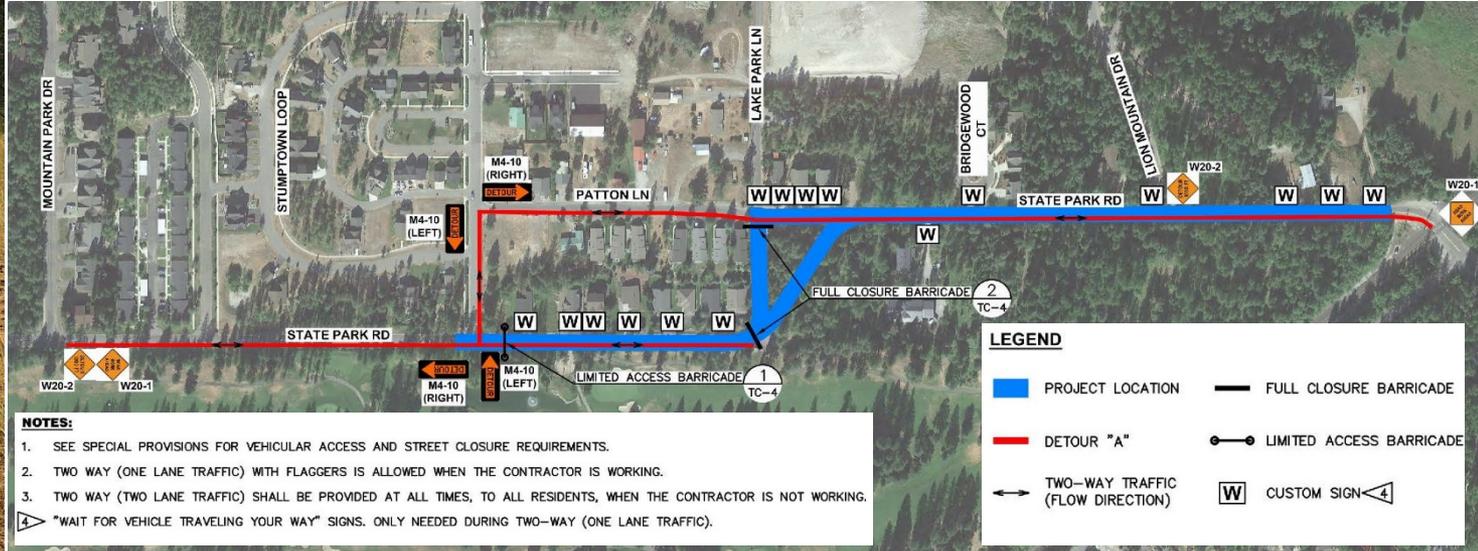



## Detour "B"

- ❑ Detour "B" will be implemented during the spring of 2020 for no more than 30 consecutive days and one day during the fall.
- ❑ Daytime travel: 2-way, 1-lane traffic with flaggers or 2-way, 2-lane traffic.
- ❑ Expect delays.
- ❑ Evening/Weekend travel: 2-way, 2-lane traffic.

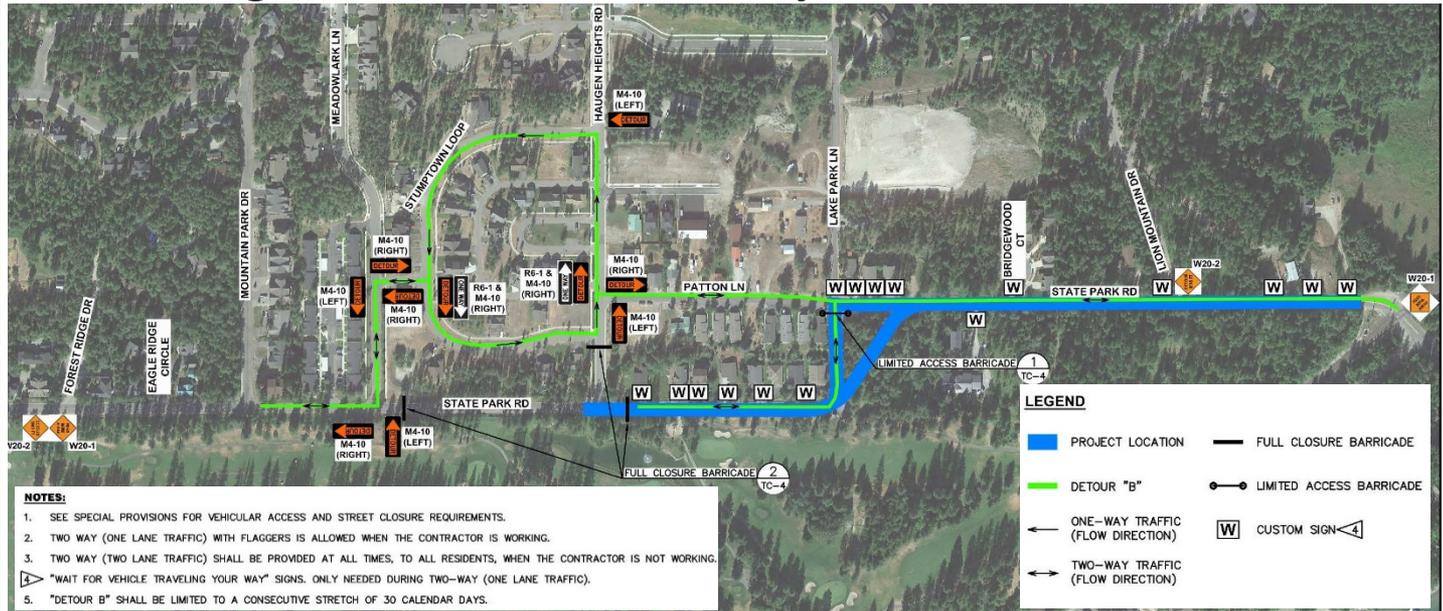



# USPS Mail Delivery during Construction

- **About 19 State Park Road mailboxes will NOT receive mail service during construction.**
- **Mail will be held at the Whitefish Post Office.**
- **New mailboxes will be provided at the end of construction.**
- **Old mailboxes will be returned to the property owner.**

## State Park Road – Phase II

Address List for USPS Mail Holdings during 2020 Construction

1. 714 State Park Road
2. 746 State Park Road
3. 760 State Park Road
4. 810 State Park Road
5. 820 State Park Road
6. 830 State Park Road
7. 840 State Park Road
8. 850 State Park Road
9. 270 Lake Park Lane
10. 295 Lake Park Lane
11. 1018 State Park Road
12. 1020 State Park Road
13. 1022 State Park Road
14. 1024 State Park Road
15. 1026 State Park Road
16. 1035 State Park Road
17. 1310 A State Park Road
18. 1310 B State Park Road
19. 22 Churmage Lane





# Future Public Communications

- **Newsletters**
- **Public Meetings**
  - ▣ One last meeting is planned before construction starts
- **City's Website**
  - ▣ Public Works Department page





# Let Us Hear From You!

- **Concerns**
  - ▣ Let us know – You live here!
- **Sign-in Sheet**
  - ▣ Please sign the Sign-in sheet
- **Comments**
  - ▣ Please complete Comment Sheets

